

Work Order ID 150395***150395***

Page 1

Wednesday, August 24, 2016 11:50:37 AM

Item ID: D5149-043W

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: Aft Step Base Assembly Weldment

Start Date: 8/22/2016 Start Qty: 2.00

Cust Item ID:

Required Date: 8/29/2016 Req'd Qty: 2.00

Customer:

Reference:

Approvals:

Process Plan:

DAS
21
9-89

Date: AUG 24 2016

Tooling:

Date:

QC:

Date:

SPC (Y/N):

Date:

Run Start

NR1

Stop

NR2

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
Draw Nbr	Revision Nbr								
D5149	D								

110 Weld per dwg A/R Aluminum rod Batch: 1121317 0.00***110***

Large Fab

Memo

0.21

Large Fab

USE DT10135 WELDING FIXTURE TO WELD D5149-043

6 02 16-9-9

120

QC9- Inspect visual per QSI004- Fusion Welds

0.00

120

QC

Memo

0.00

Quality Control

6 0 16-09-12

130

QC5- Inspect part completeness to step on W/O

0.00

130

QC

Memo

0.01

Quality Control

(16) 16 16-09-12

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					

Root Cause				FAULT CATEGORY			
Environment ☐	☐	No Re-verification ☐	☐	Pressure/Forced ☐	☐	Temperature/Cure ☐	☐
Design ☐	☐	Operator ☐	☐	Bending ☐	☐	Set-up ☐	☐
Doc/Data ☐	☐	Offset/Setup ☐	☐	Centre Not Concentric ☐	☐	BOM/Route ☐	☐
Equip/Tooling ☐	☐	Supplier ☐	☐	Cracks ☐	☐	Broken/Damage/Defect ☐	☐
Handling/Pre ☐	☐	Training ☐	☐	Crimp/Kink/Ripple/Wave ☐	☐	Inspection Incomplete/Unqualified ☐	☐
Material ☐	☐	Use for Testing ☐	☐	Cuffs ☐	☐	Contamination ☐	☐
Internal Transport ☐	☐	Poor Information ☐	☐	Crushing ☐	☐	Countersink ☐	☐
Tribal Knowledge ☐	☐	Rushing ☐	☐	Heat Treat ☐	☐	Cut Too Short ☐	☐
LOA ☐	☐	Product Improvement ☐	☐	Wave/Twist in Tube ☐	☐	Instructions Incomplete/Unclear ☐	☐
Substation ☐	☐	Process Improvement ☐	☐	Marks/Chatter ☐	☐	Drill Holes ☐	☐
Past Expiry Date ☐	☐	Manufacturing Process ☐	☐	OTHER : _____ _____ _____			
Misidentified ☐	☐	Past Due ☐	☐				

Work Order ID 150395

Wednesday, August 24, 2016 11:50:37 AM

150395

Page 2

Item ID: D5149-043W Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Aft Step Base Assembly Weldment
Start Date: 8/22/2016 Start Qty: 2.00 ***2*** Cust Item ID:
Required Date: 8/29/2016 Req'd Qty: 2.00 ***2*** Customer:
Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
140	Chemical Conversion Coat per QSI005 4.1	0.00							
140	HandFinish	0.03				(x6)			2016/09/13
Hand Finishing	Memo								BEB.
150	QC7-Inspect Chemical Conversion Coat	0.00							
150	QC	0.00							6 φ 1009-13 34 9-89
Quality Control	Memo								
160	White Gloss(Ref:4.3.5.1) per QSI005 4.3-Alum	0.00							
160	Powdercoat	0.02							6 φ 16-09-13 34 9-89
Powder Coating	Memo								
	START TIME: 11:00								
	OVEN TEMPERATURE: 320°								
	FINISH TIME: 11:30								

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE



QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐
OTHER : _____					

Wednesday, August 24, 2016 11:50:37 AM

150395

Page 3

N900040100

Setup Start *NS1*

Stop *NS2*

~

Cust Item ID:

Start Date: 8/22/2016 **Start Qty:** 2.00

~

Customer:

Reference:

Run Start *NR1*

Approvals: **Process Plan:** _____ **Date:** _____ **Tooling:** _____ **Date:** _____

Stop *NR2*

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

**Insp.
Stamp**

170

QC3- Inspect Part Finish

0.00

170

QC

Memo

0.00

Quality Control

180

Wing Walk as per dwg QSI005 4.4 Batch M13550

0.00

180

HandFinish

Memo

0.03

Hand Finishing

190

QC3- Inspect Part Finish

0.00

190

QC

Memo

0.00

Quality Control

DAS
 15
 7-89

38
9-89

SEP 14 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : _____					

Work Order ID 150395

Wednesday, August 24, 2016 11:50:37 AM

150395

Page 4

Item ID: D5149-043W

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: Aft Step Base Assembly Weldment

Start Date: 8/22/2016 Start Qty: 2.00

2

Cust Item ID:

Required Date: 8/29/2016 Req'd Qty: 2.00

2

Customer:

Reference:

Approvals:

Process Plan:

Date:

Tooling:

Date:

Run Start

NR1

QC:

Date:

SPC (Y/N):

Date:

Stop

NR2Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

200

Identify as per dwg & Stock Location: W/6

0.00

200

Packaging

Memo

146877

0.00

Packaging

6x16/09/22DAS
36
9-89

210

QC21- Final Inspection - Work Order Release

0.00

210

QC

Memo

0.03

Quality Control

DAS
21
9-89

SEP 22 2016

DAS
21
9-89

SEP 22 2016

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE



QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐
OTHER :					

Picklist Print

Wednesday, August 24, 2016 11:50:37 AM

Page 1

Work Order ID: 150395

150395

Parent Item: D5149-043W

D5149-043W

Parent Item Name: Aft.Step Base Assembly Weldment

Start Date: 8/22/2016

Required Date: 8/29/2016

Start Qty: 2.00

Required Qty: 2.00

Comments: IPP REV:A 14.12.15 NEW ISSUE DD VERF;JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D5149-5 *D5149-5* Step Cap		Manufactured	No				Each	27.0000		2			
					<u>Location</u>	<u>Loc Qty</u>		<u>Loc Code</u>					
					WA001	27							
					145680	27							
D5149-7 *D5149-7* Aft Step Base		Manufactured	No				Each	19.0000		2			
					<u>Location</u>	<u>Loc Qty</u>		<u>Loc Code</u>					
					WA004	19							
					148143	10							
					148538	9							
D5149-9 *D5149-9* Aft Step		Manufactured	No				Each	17.0000		2			
					<u>Location</u>	<u>Loc Qty</u>		<u>Loc Code</u>					
					WA001	17							
					146925	7							
					147978	10							

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE





QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : ☐					

ITEM	QTY	P/N	DESCRIPTION
	X	D5149-041	FWD STEP ASSEMBLY
1	1	D5149-041W	FWD STEP BASE WELDMENT
2	1	D5151-1	CLAMP CUSHION

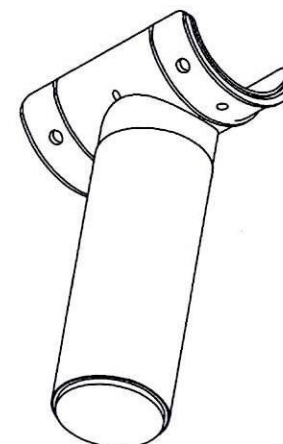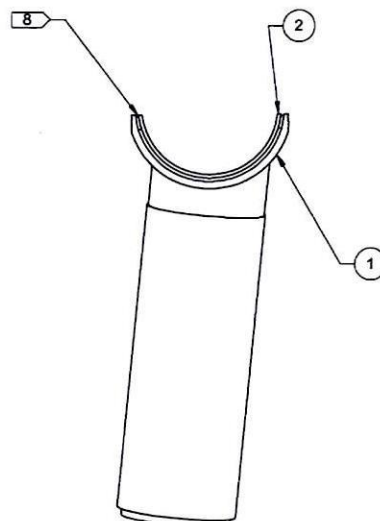

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 150395 MJS
16-08-29

D5149-041 FWD STEP ASSEMBLY



NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: IDENTIFY PER QSI 044 6.1
- 7) WEIGHT: 0.69 lbs
- 8) BOND D5151-1 CUSHION TO D5149-041W BASE WELDMENT USING 3M 1300L ADHESIVE

D	DIAMETER OF D5149-5 CAP IS NOW 1.88 WAS 2.00 TO EASE WELDING PROCEDURE. UPDATE TOLERANCES	AP	15.10.20
C	ANTI-KID FINISH DIM MODIFIED DUE TO INTERFERENCE WITH WELD (SHT 3 & 4)	AP	15.04.27
B	COMPLETE RE-DESIGN, SEE PREVIOUS REV FOR DETAILS	DB	15.01.14
A	NEW ISSUE	DB	14.10.25
REV.	DESCRIPTION	BY	DATE
DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AP		
CHECKED	DB		
MFG. APPR.	DD		
APPROVED	WM		
DE APPR.	DS	STEP ASSEMBLY	
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

RELEASED
2015-11-04
EN 15-142

ITEM	QTY -043	P/N	DESCRIPTION
	X	D5149-043	AFT STEP ASSEMBLY
1	1	D5149-043W	AFT STEP BASE WELDMENT
2	1	D5151-3	CLAMP CUSHION

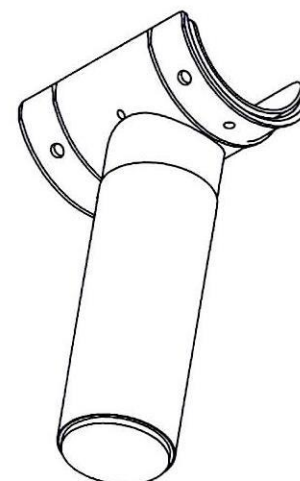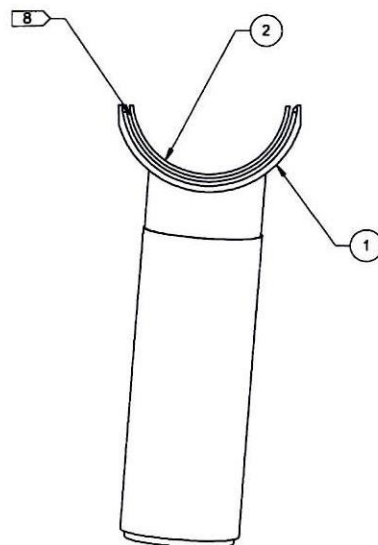

D5149-043 AFT STEP ASSEMBLY

NOTES:


- 1) MATERIAL: N/A
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: IDENTIFY PER QSI 044 6.1
- 7) WEIGHT: 0.87 lbs
- 8) BOND D5151-3 CUSHION TO D5149-043W BASE WELDMENT USING 3M 1300L ADHESIVE

RELEASED
2015-11-04

APPROVED

DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AP		
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 2 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS COVENANT THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

ITEM	QTY-041W	P/N	DESCRIPTION
	X	D5149-041W	FWD STEP BASE WELDMENT
1	1	D5149-1	FWD STEP BASE
2	1	D5149-3	FWD STEP
3	1	D5149-5	STEP CAP

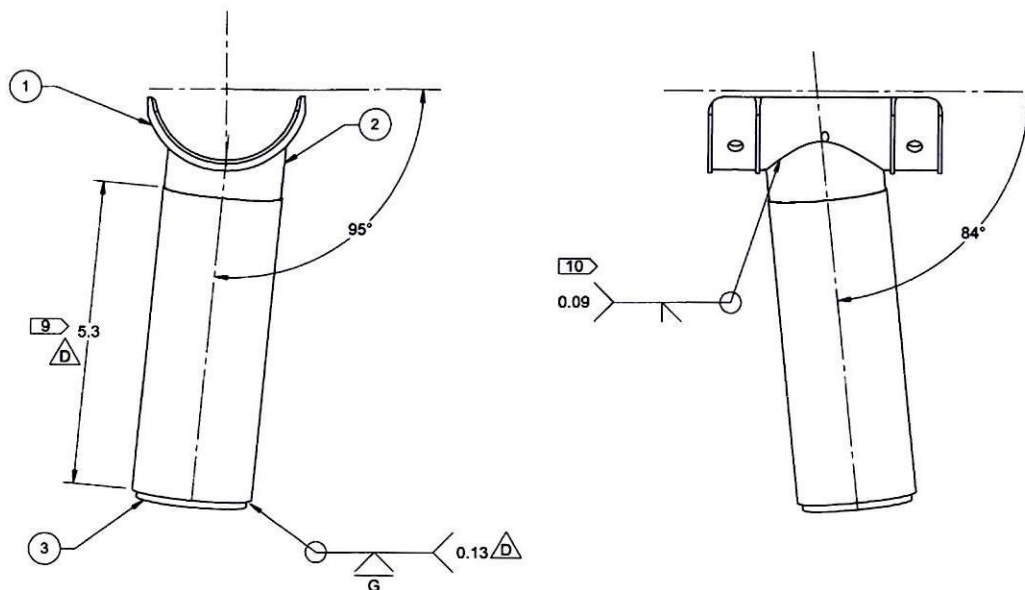

D5149-041W FWD STEP BASE WELDMENT

NOTES:


- 1) MATERIAL: N/A
- 2) FINISH: CHEMICAL CONVERSION COAT PER DART QSI 005 4.1
POWDER COAT "WHITE" (4.3.5.1) PER DART QSI 005 4.3
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.67 lbs
- 8) WELDING PER DART QSI 004
- 9) APPLY BLACK ANTI-SKID PAINT TO STEP TUBE, ALL AROUND PER DART QSI 005 4.4
- 10) ALIGN D5149-3 FWD STEP WITH EDGE OF ALIGNMENT HOLES IN D5149-1 FWD STEP BASE PRIOR TO WELDING

RELEASED
2015-11-04

APPROVED

DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AP		
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 3 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD	

ITEM	QTY-043W	P/N	DESCRIPTION
	X	D5149-043W	AFT STEP BASE WELDMENT
1	1	D5149-5	STEP CAP
2	1	D5149-7	AFT STEP BASE
3	1	D5149-9	AFT STEP

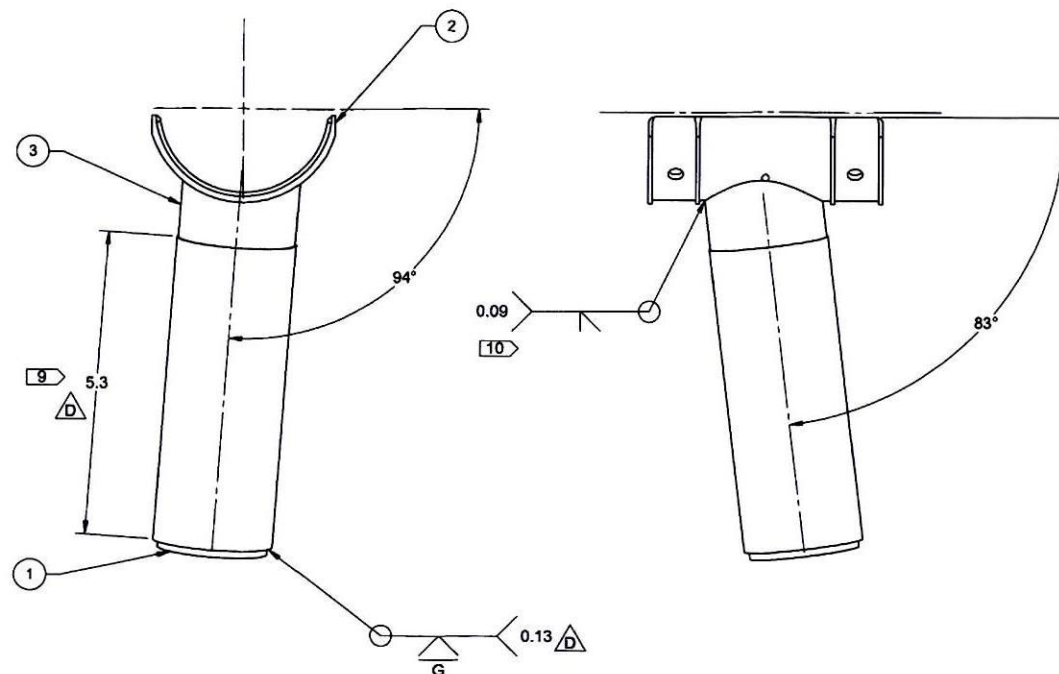

D5149-043W AFT STEP BASE WELDMENT


NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: CHEMICAL CONVERSION COAT PER DART QSI 005 4.1
POWDER COAT "WHITE" (4.3.5.1) PER DART QSI 005 4.3
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.67 lbs
- 8) WELDING PER DART QSI 004
- 9) APPLY BLACK ANTI-SKID PAINT TO STEP TUBE, ALL AROUND PER DART QSI 005 4.4
- 10) ALIGN D5149-9 AFT STEP WITH EDGE OF ALIGNMENT HOLES IN D5149-7 AFT STEP BASE PRIOR TO WELDING


RELEASED
2015-11-04

APPROVED

DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AP		
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 4 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL, AND IS SUPPLIED ON THE EXPRESS UNDERSTANDING THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

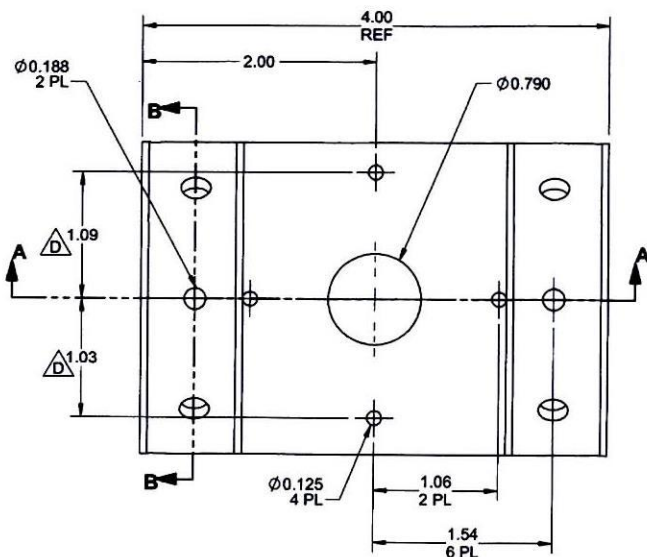


D5149-1 FWD STEP BASE
(MAKE FROM D5149-1TRN)




SECTION A-A

0.06 X 45° CMF
ALL AROUND INSIDE EDGE

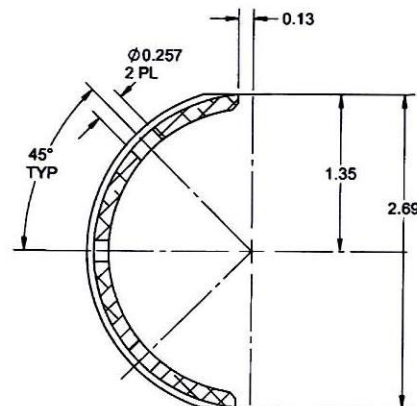

SECTION B-B
2 PL






NOTES:

- 1) MATERIAL: MAKE FROM D5149-1TRN
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.20 lbs

RELEASED
2015-11-04

APPROVED

DESIGN	DB	DART AEROSPACE LTD	
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 5 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			

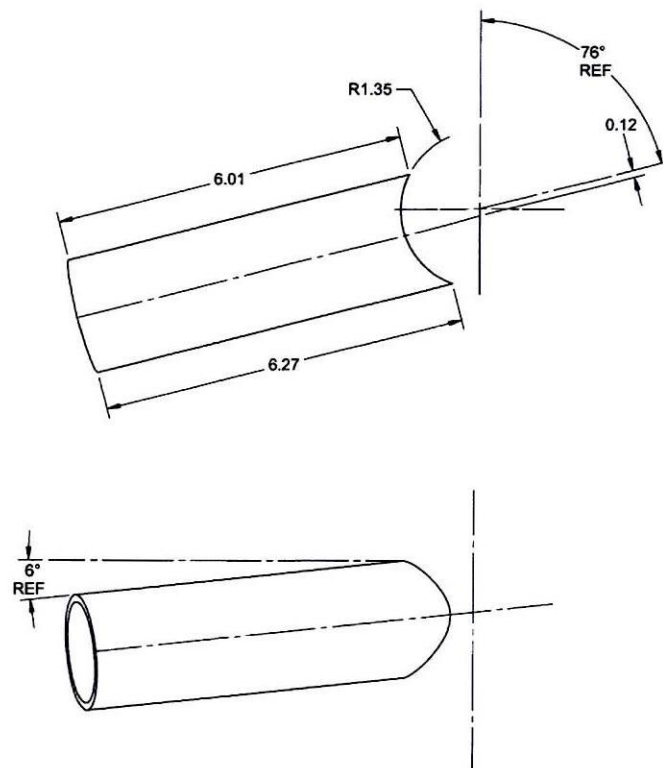

D5149-3 FWD STEP



NOTES:

- 1) MATERIAL: 6061-T6/T62/T6510/T6511 SEAMLESS TUBING PER WW-T-700/6 OR QQ-A-200/8 OR QQ-A-225/8 OR AMS 4080 OR AMS 4082 OR AMS 4083 OR ASTM B210 OR ASTM B241
REF DART SPEC M6061T6T2.000W0.125
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.42 lbs

RELEASED
2015 -11- 04

APPROVED

DESIGN	DB	DART AEROSPACE LTD	
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 6 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD			

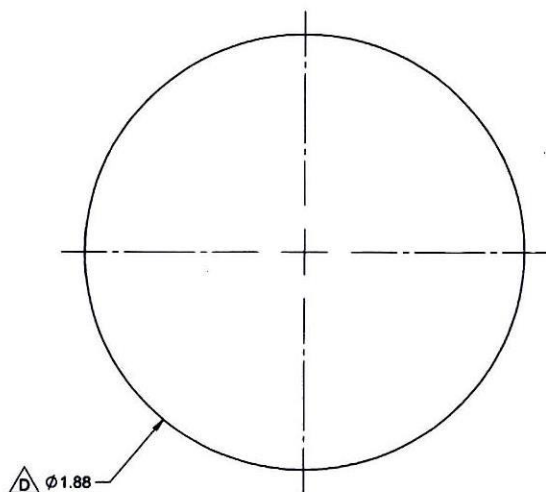

D5149-5 STEP CAP


NOTES:


- 1) MATERIAL: 6061-T6 (OR 6061-T62) ALUMINUM SHEET, 0.125 THICK
PER QQ-A-250/11 OR AMS-QQ-A-250/11 OR AMS 4025 OR ASTM B209
REF DART SPEC M6061T6S.125
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.03 lbs

RELEASED
2015-11-04

APPROVED

DESIGN	DB	DART AEROSPACE LTD		
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA		
CHECKED	DB	DRAWING NO.		REV. D
MFG. APPR.	DD	D5149		SHEET 7 OF 11
APPROVED	WM	TITLE		SCALE
DE APPR.	DS	STEP ASSEMBLY		NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD		
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL, AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.				

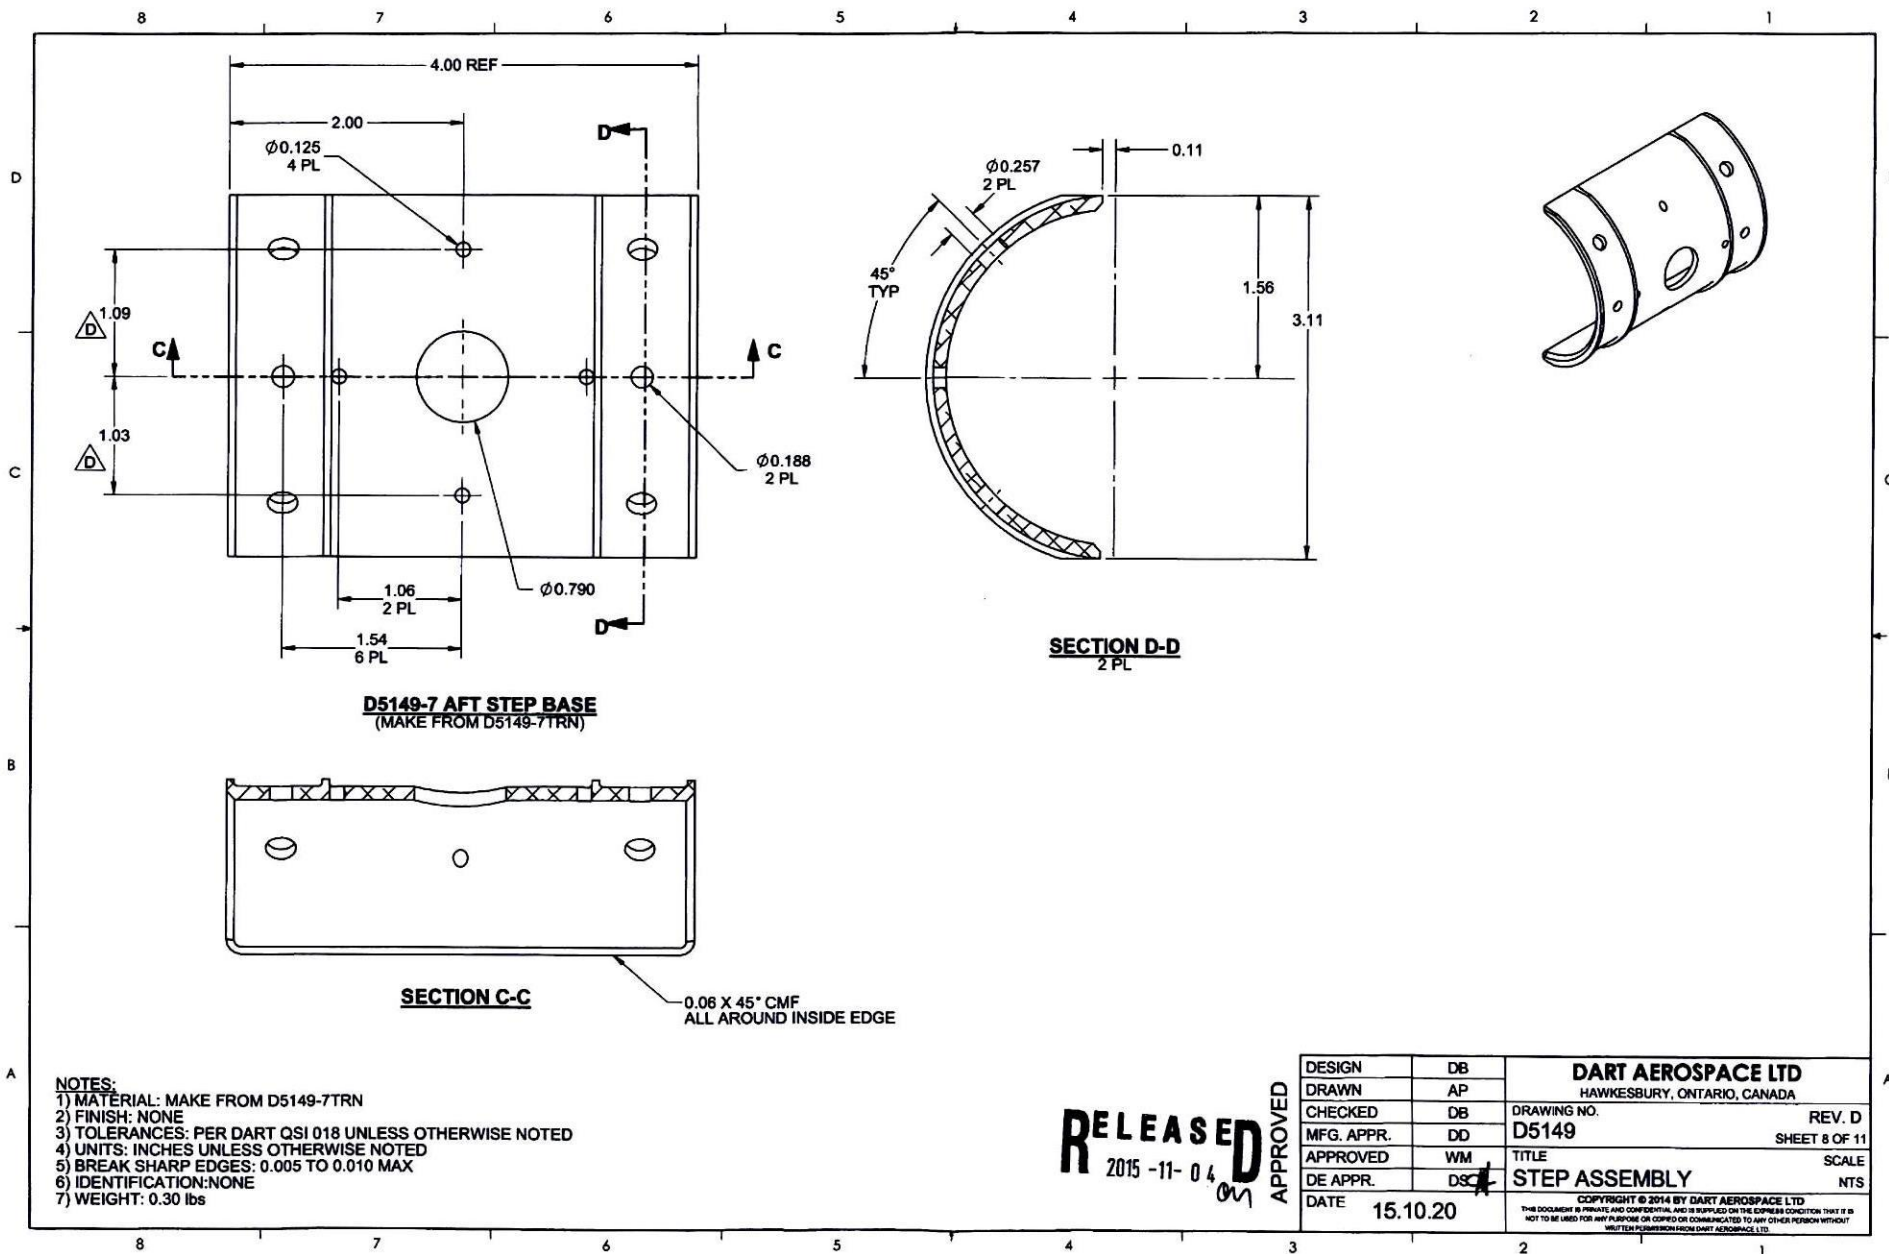

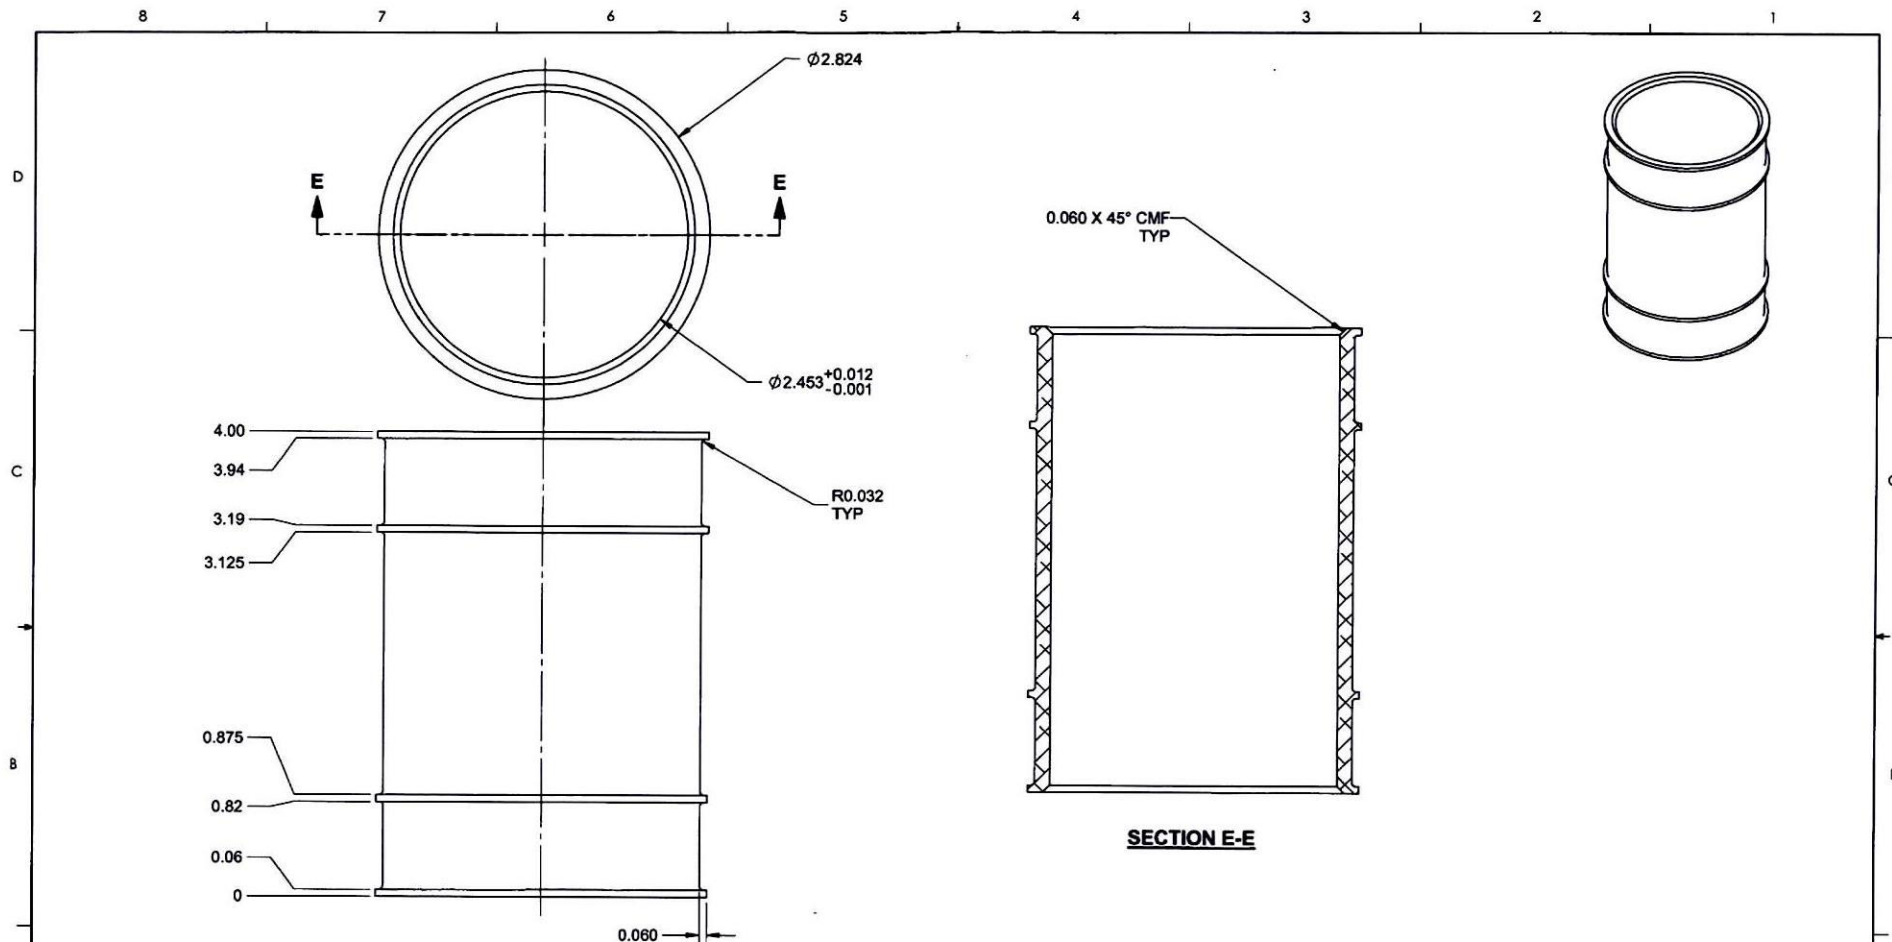

D5149-1TRN TURNING DETAIL


NOTES:

- 1) MATERIAL: 6061-T6/T651/T6510/T6511/T62 ALUMINUM ROUND BAR
PER QQ-A-225/8 OR AMS-QQ-A-225/8 (OR AMS 4117/4128/4115/4116)
OR QQ-A-200/8 OR AMS-QQ-200/8 (OR AMS 4160) OR ASTM B211 OR ASTM B221
REF DART SPEC. M6061T6R
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.41 lbs

RELEASED
2015-11-04

APPROVED

DESIGN	DB	DART AEROSPACE LTD	
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 9 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD			

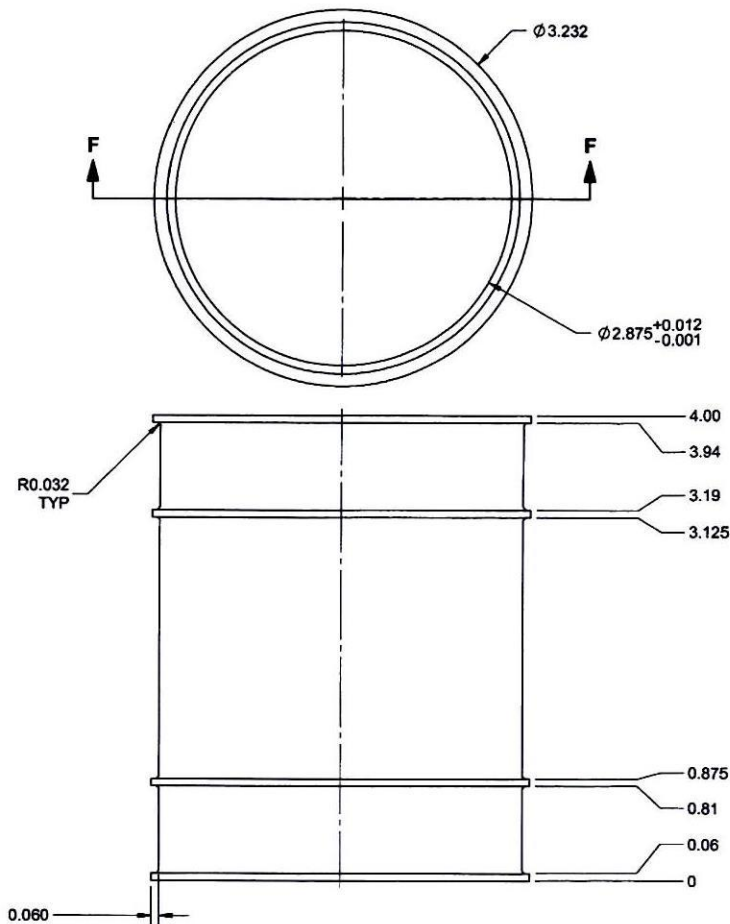

D5149-7TRN TURNING DETAIL


NOTES:

- 1) MATERIAL: 6061-T6/T651/T6510/T6511/T62 ALUMINUM ROUND BAR
PER QQ-A-225/8 OR AMS-QQ-A-225/8 (OR AMS 4117/4128/4115/4116)
OR QQ-A-200/8 OR AMS-QQ-200/8 (OR AMS 4160) OR ASTM B211 OR ASTM B221
REF DART SPEC. M6061T6R
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.41 lbs




RELEASED
2015-11-04

APPROVED

DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AP		
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 10 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

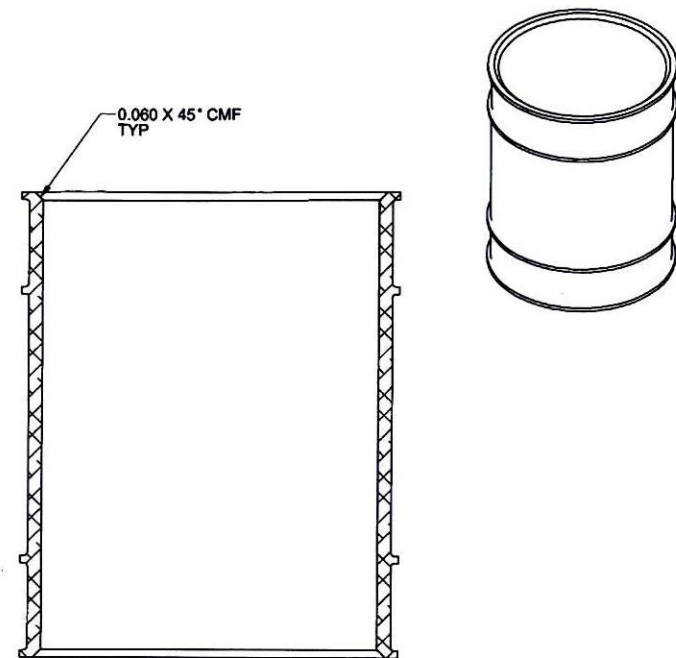

SECTION F-F

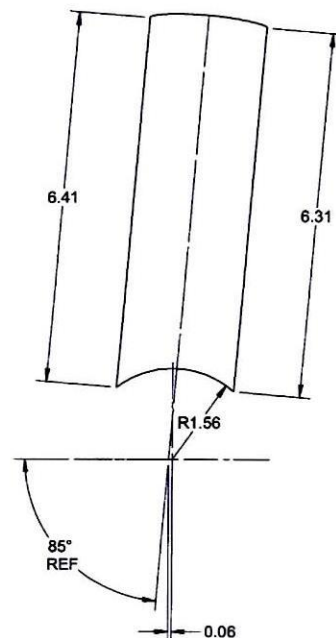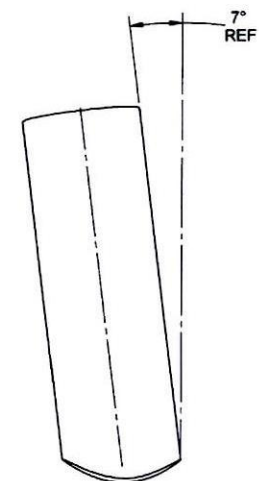

D5149-9 AFT STEP

NOTES:

- 1) MATERIAL: 6061-T6/T62/T6510/T6511 SEAMLESS TUBING PER WW-T-700/6 OR QQ-A-200/8 OR QQ-A-225/8 OR AMS 4080 OR AMS 4082 OR AMS 4083 OR ASTM B210 OR ASTM B241
REF DART SPEC M6061T6T2.000W0.125
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.44 lbs

RELEASED
2015-11-04

APPROVED

DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AP		
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 11 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR DISCLOSED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	
